



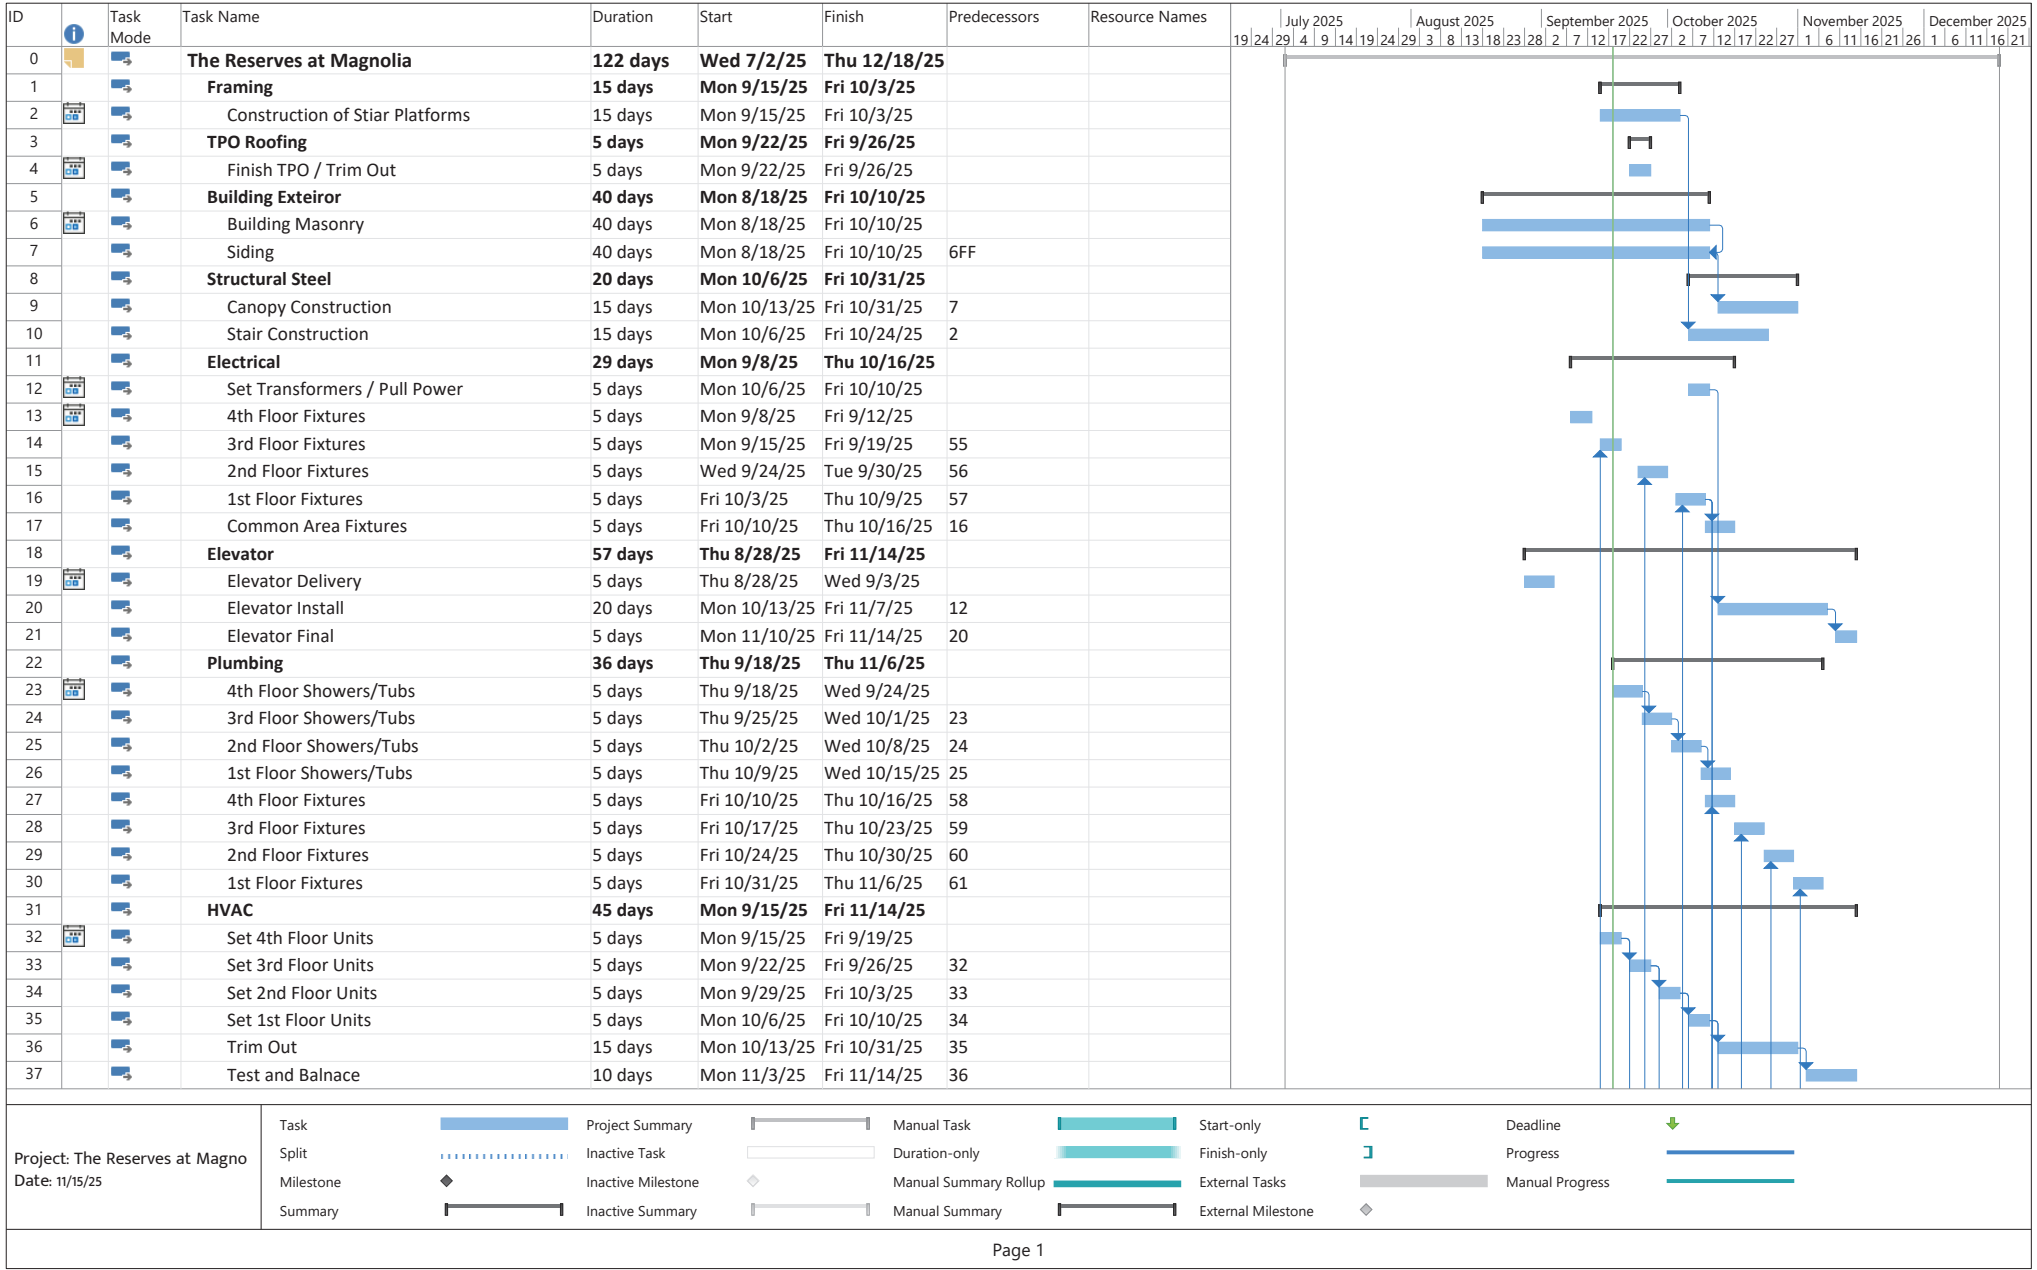

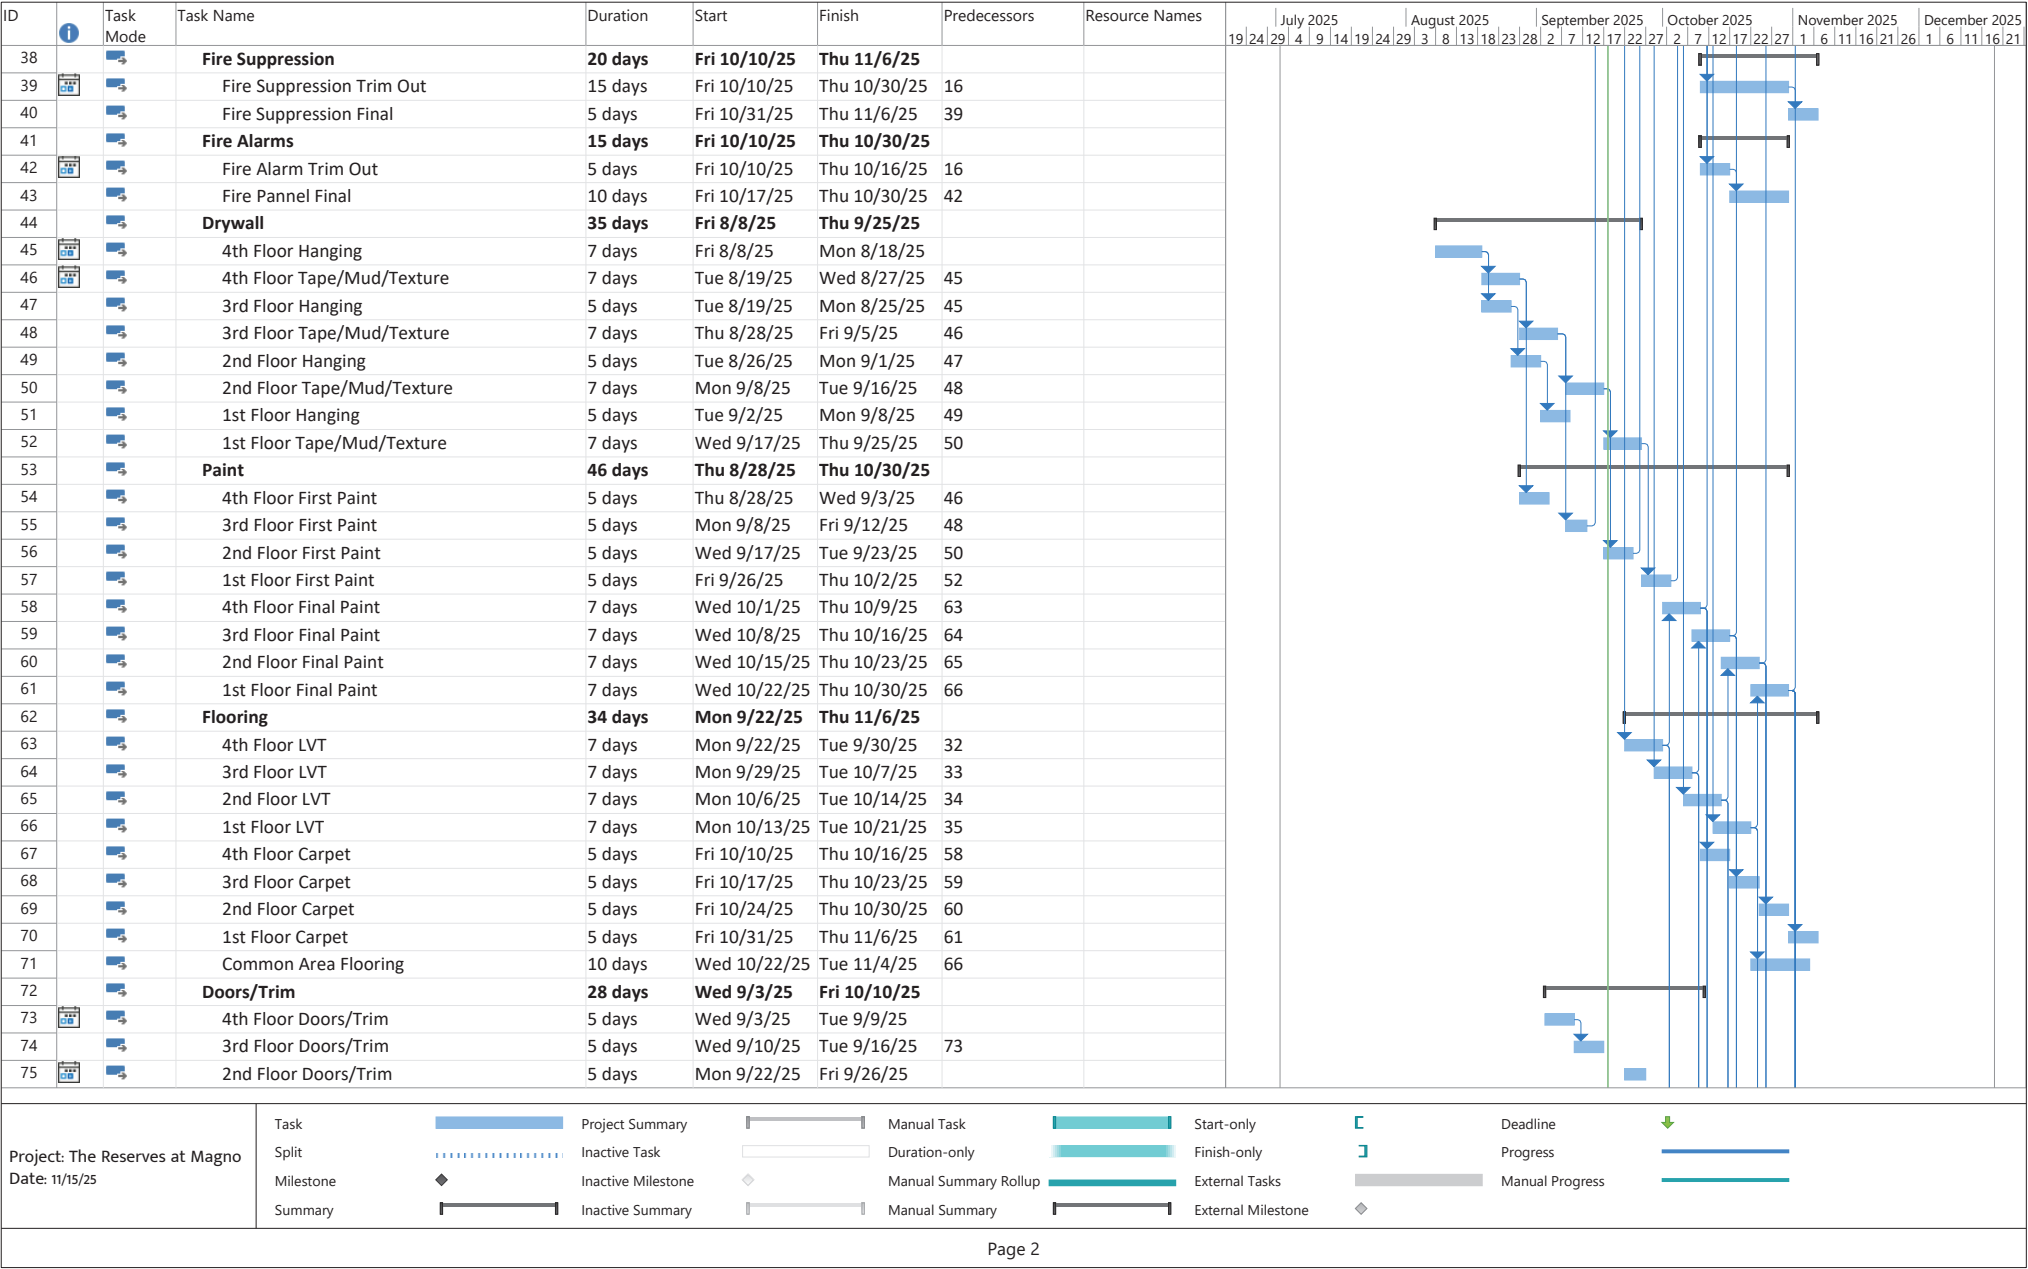

[illegible]

Project: The Reserves at Magno Date: 11/15/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

[illegible]

Project: The Reserves at Magno Date: 11/15/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	July 2025							August 2025							September 2025							October 2025							November 2025							December 2025						
152		2nd Floor Finals	0 days	Thu 11/6/25	Thu 11/6/25	163		19	24	29	4	9	14	19	24	29	3	8	13	18	23	28	2	7	12	17	22	27	2	7	12	17	22	27	1	6	11	16	21	26	1	6	11	16	21				
153		1st Floor Finals	0 days	Thu 11/13/25	Thu 11/13/25	166																																											
154		Site Finals	0 days	Tue 10/28/25	Tue 10/28/25	133SF+15 days																																											
155		Certification of Occupancy Window	15 days	Fri 11/14/25	Thu 12/4/25	153																																											
156		Punch	31 days	Fri 10/17/25	Fri 11/28/25																																												
157		4th Floor Punch	5 days	Fri 10/17/25	Thu 10/23/25	93																																											
158		4th Floor Punch Corrections	10 days	Fri 10/24/25	Thu 11/6/25	157																																											
159		4th Floor Re-Punch	1 day	Fri 11/7/25	Fri 11/7/25	158																																											
160		3rd Floor Punch	5 days	Fri 10/24/25	Thu 10/30/25	94																																											
161		3rd Floor Punch Corrections	10 days	Fri 10/31/25	Thu 11/13/25	160																																											
162		3rd Floor Re-Punch	1 day	Fri 11/14/25	Fri 11/14/25	161																																											
163		2nd Floor Punch	5 days	Fri 10/31/25	Thu 11/6/25	95																																											
164		2nd Floor Punch Corrections	10 days	Fri 11/7/25	Thu 11/20/25	163																																											
165		2nd Floor Re-Punch	1 day	Fri 11/21/25	Fri 11/21/25	164																																											
166		1st Floor Punch	5 days	Fri 11/7/25	Thu 11/13/25	96																																											
167		1st Floor Punch Corrections	10 days	Fri 11/14/25	Thu 11/27/25	166																																											
168		1st Floor Re-Punch	1 day	Fri 11/28/25	Fri 11/28/25	167																																											
169		Turn-Over	5 days	Fri 12/5/25	Thu 12/11/25																																												
170		Building Turn-Over Window	5 days	Fri 12/5/25	Thu 12/11/25	155																																											
171		Items to Notes/Plan For	122 days	Wed 7/2/25	Thu 12/18/25																																												

Project: The Reserves at Magno Date: 11/15/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
