


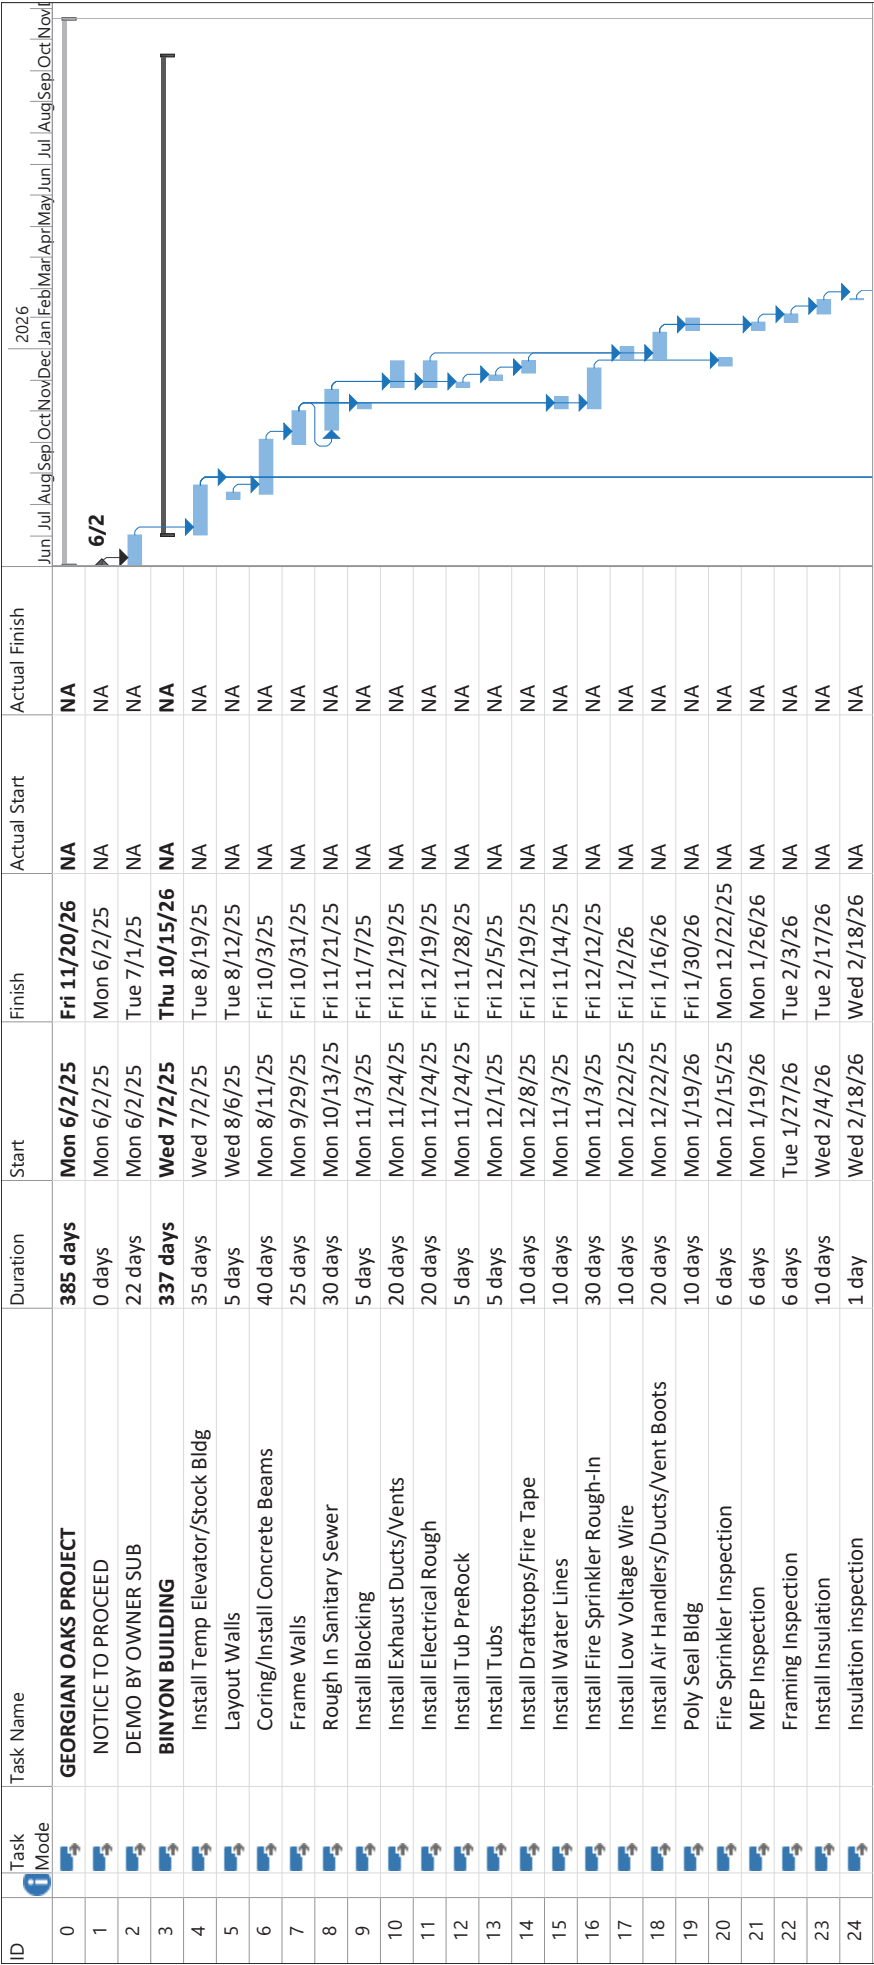

Project: GEORGIAN OAKS PROJ
Date: Thu 5/22/25

Task

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


External Milestone

Deadline


Progress


Manual Progress


Page 1

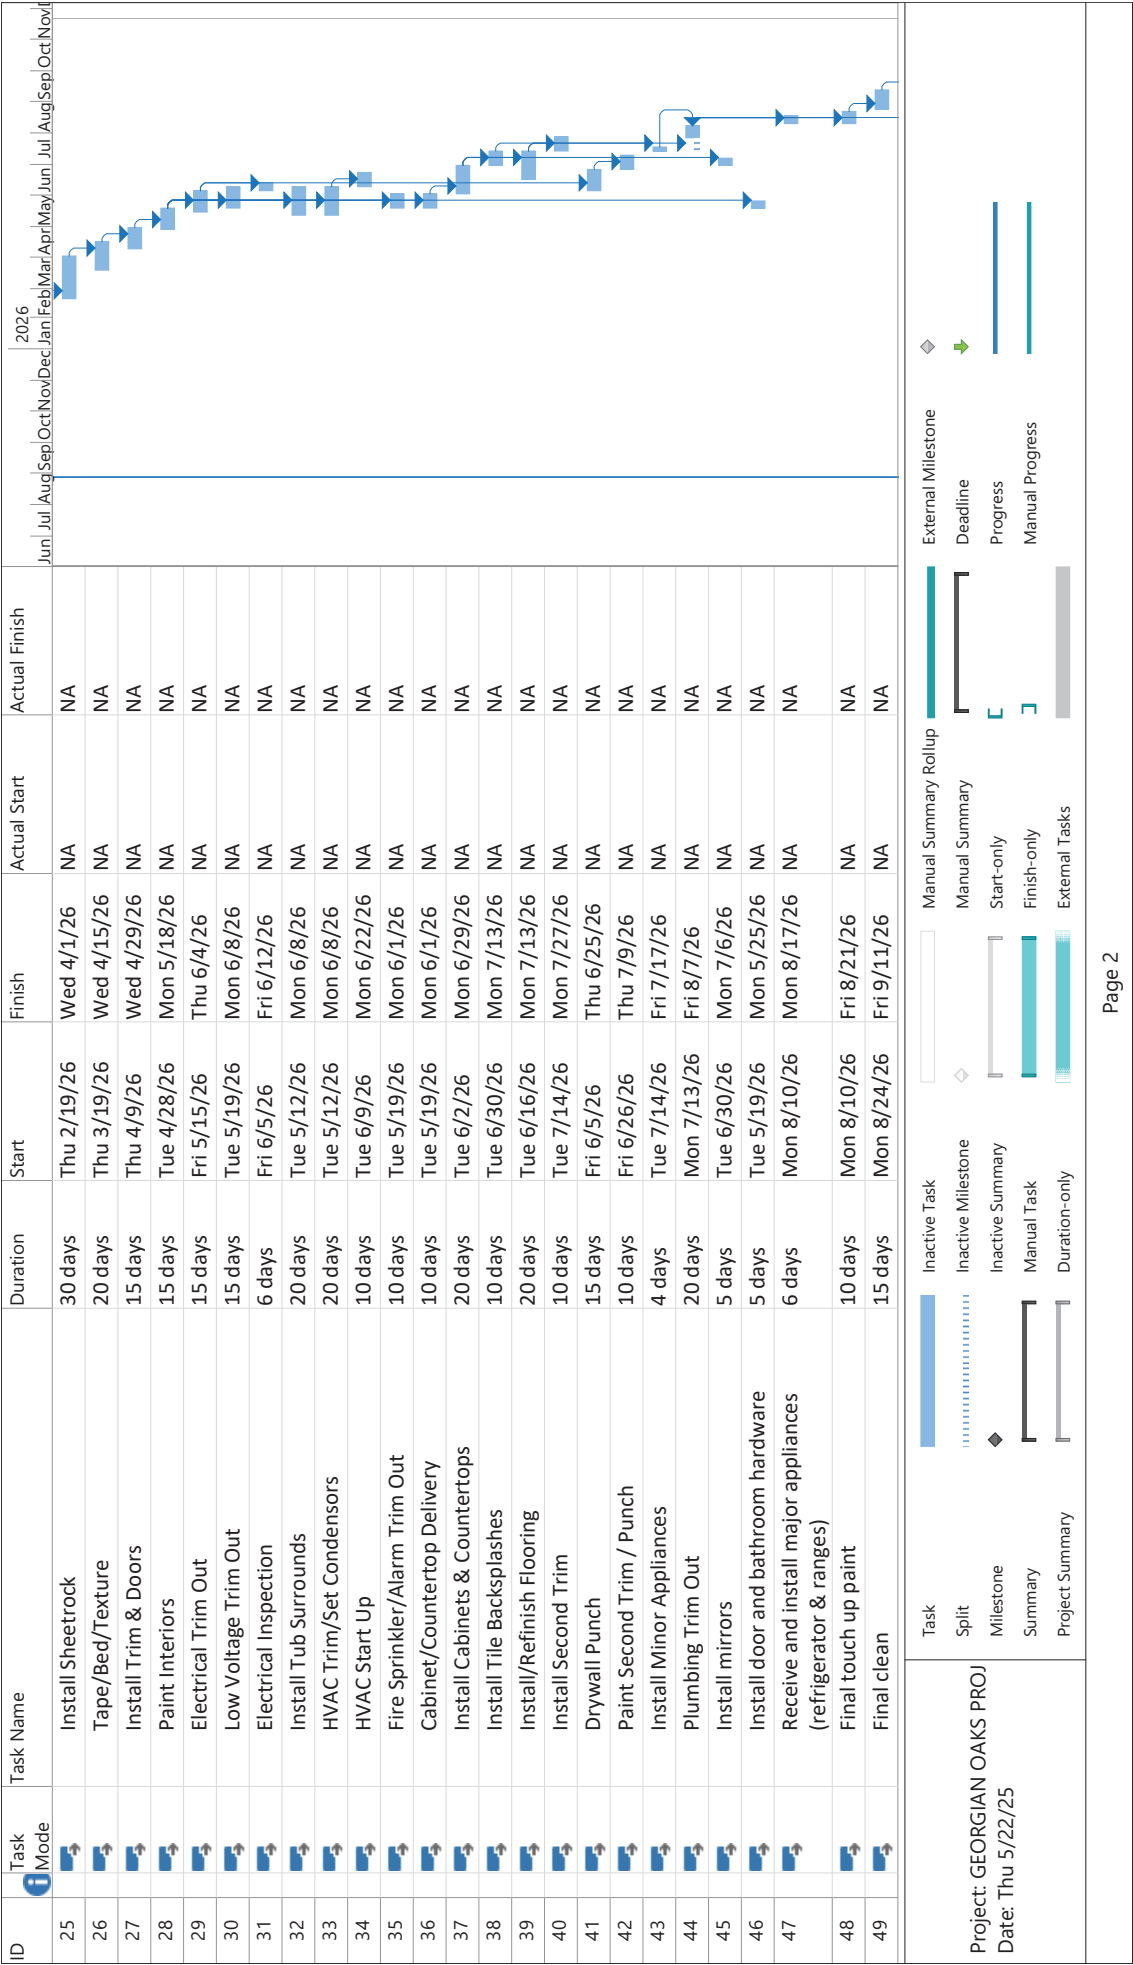
External MilestoneDeadlineProgressManual Progress

Page 2

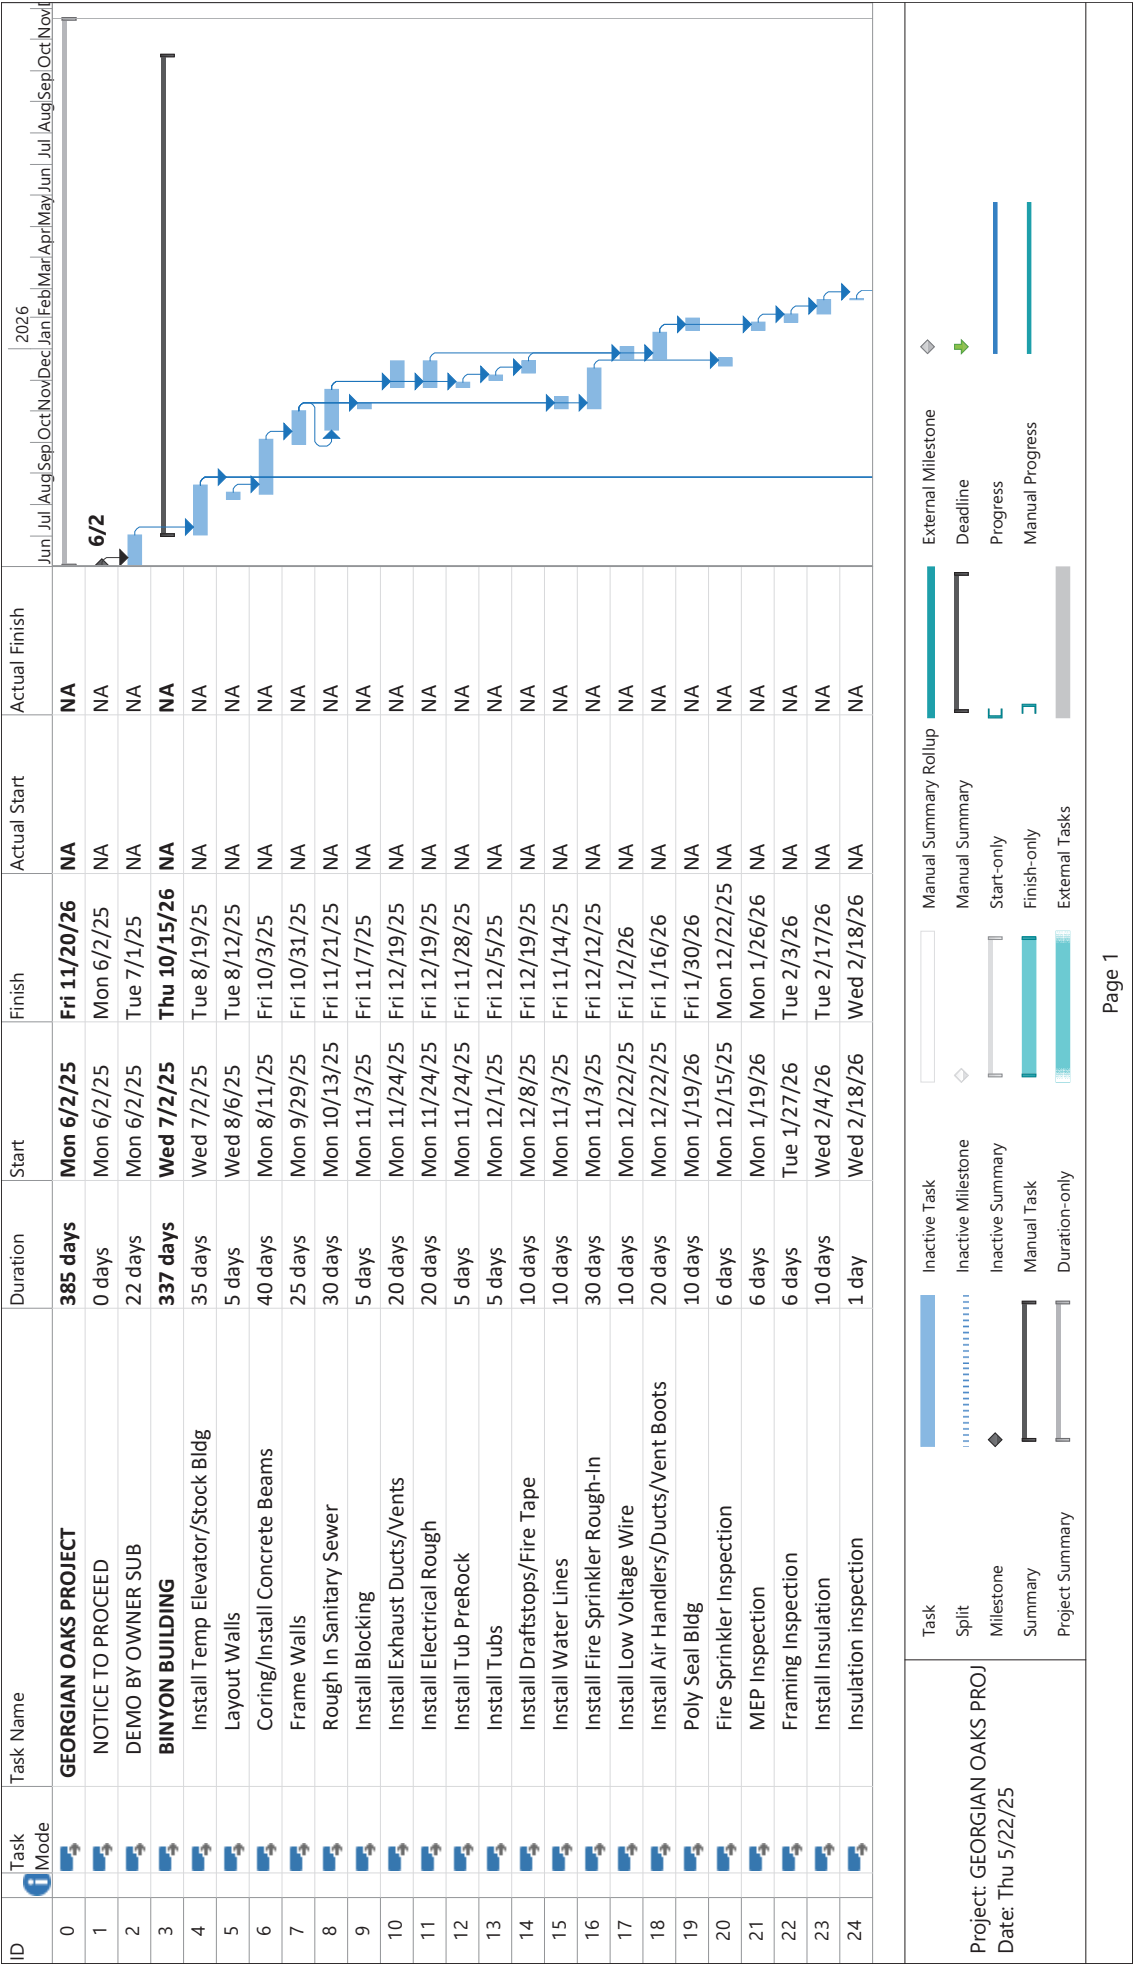

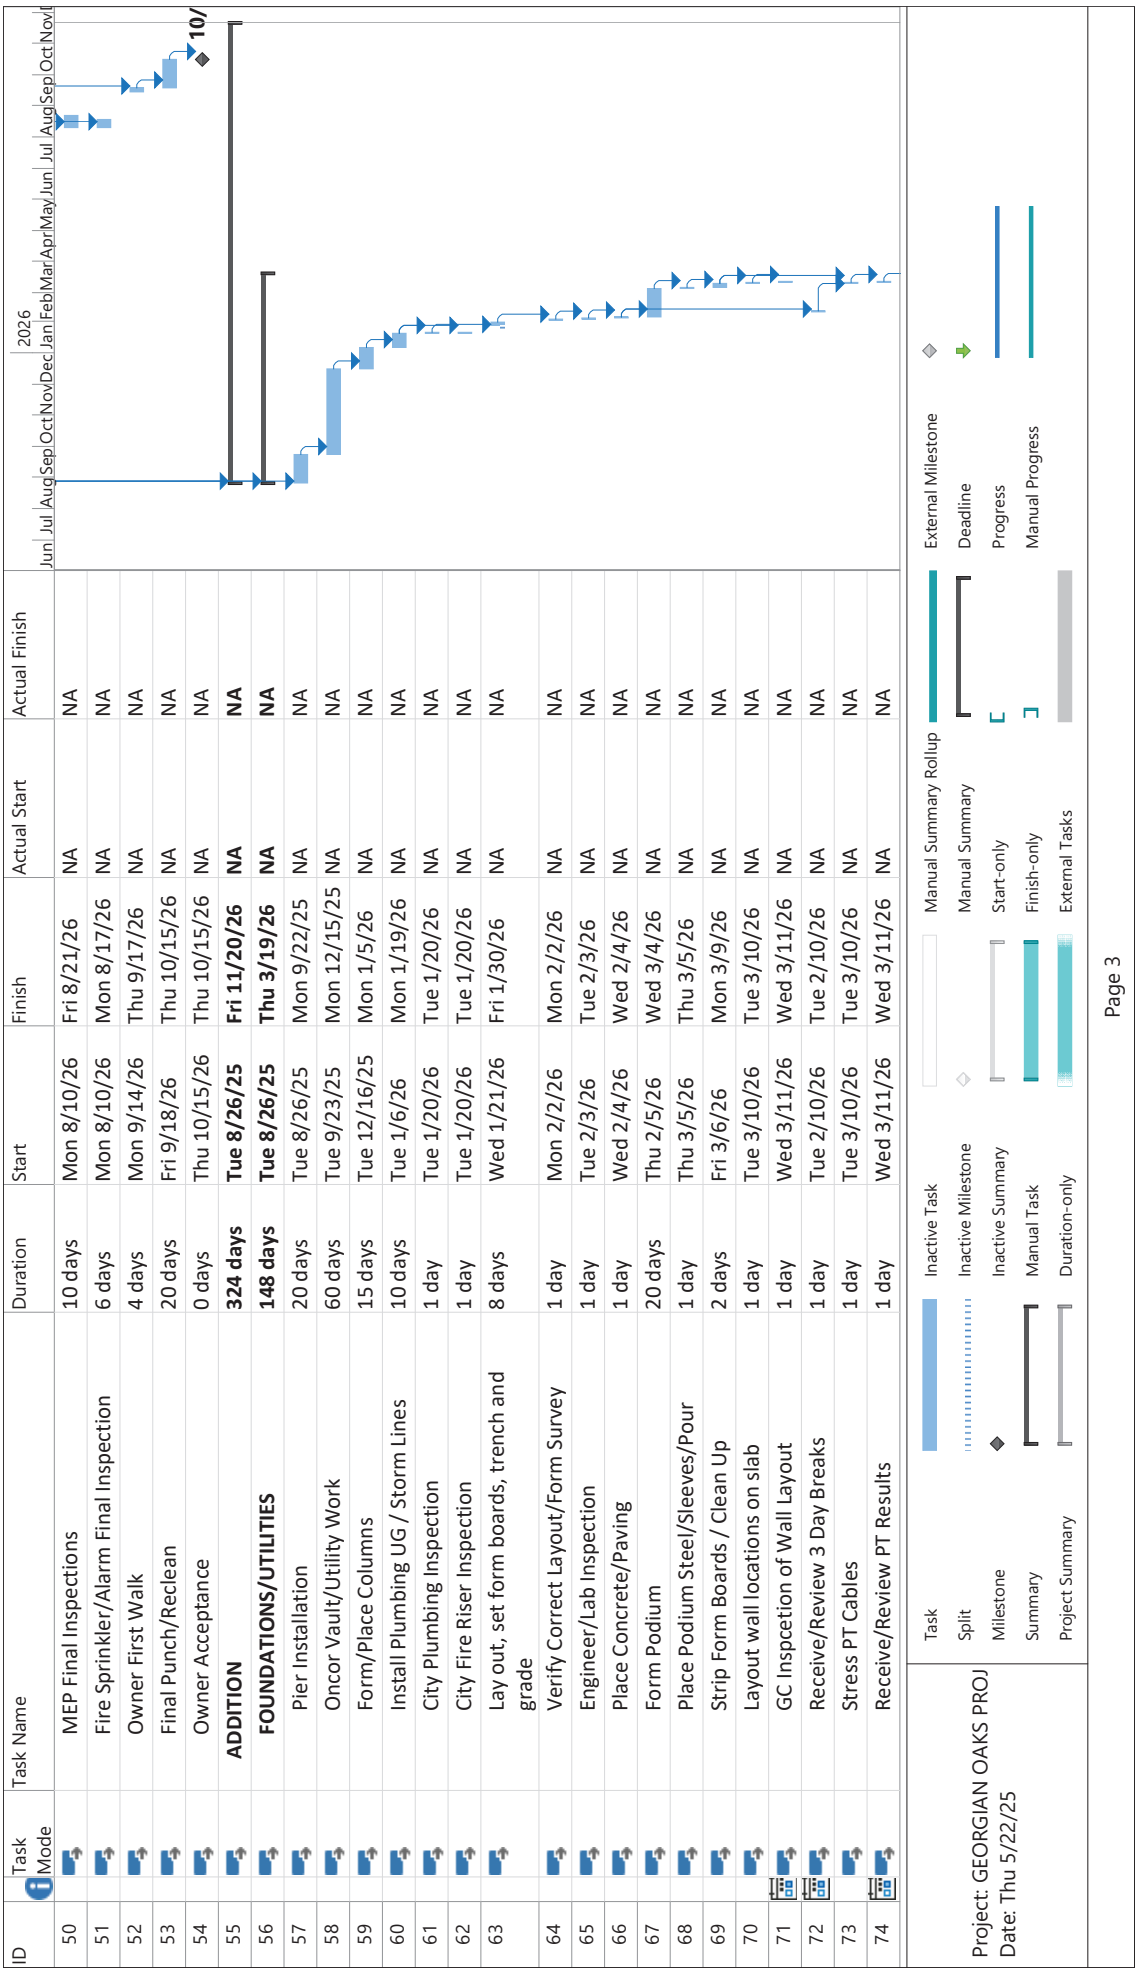

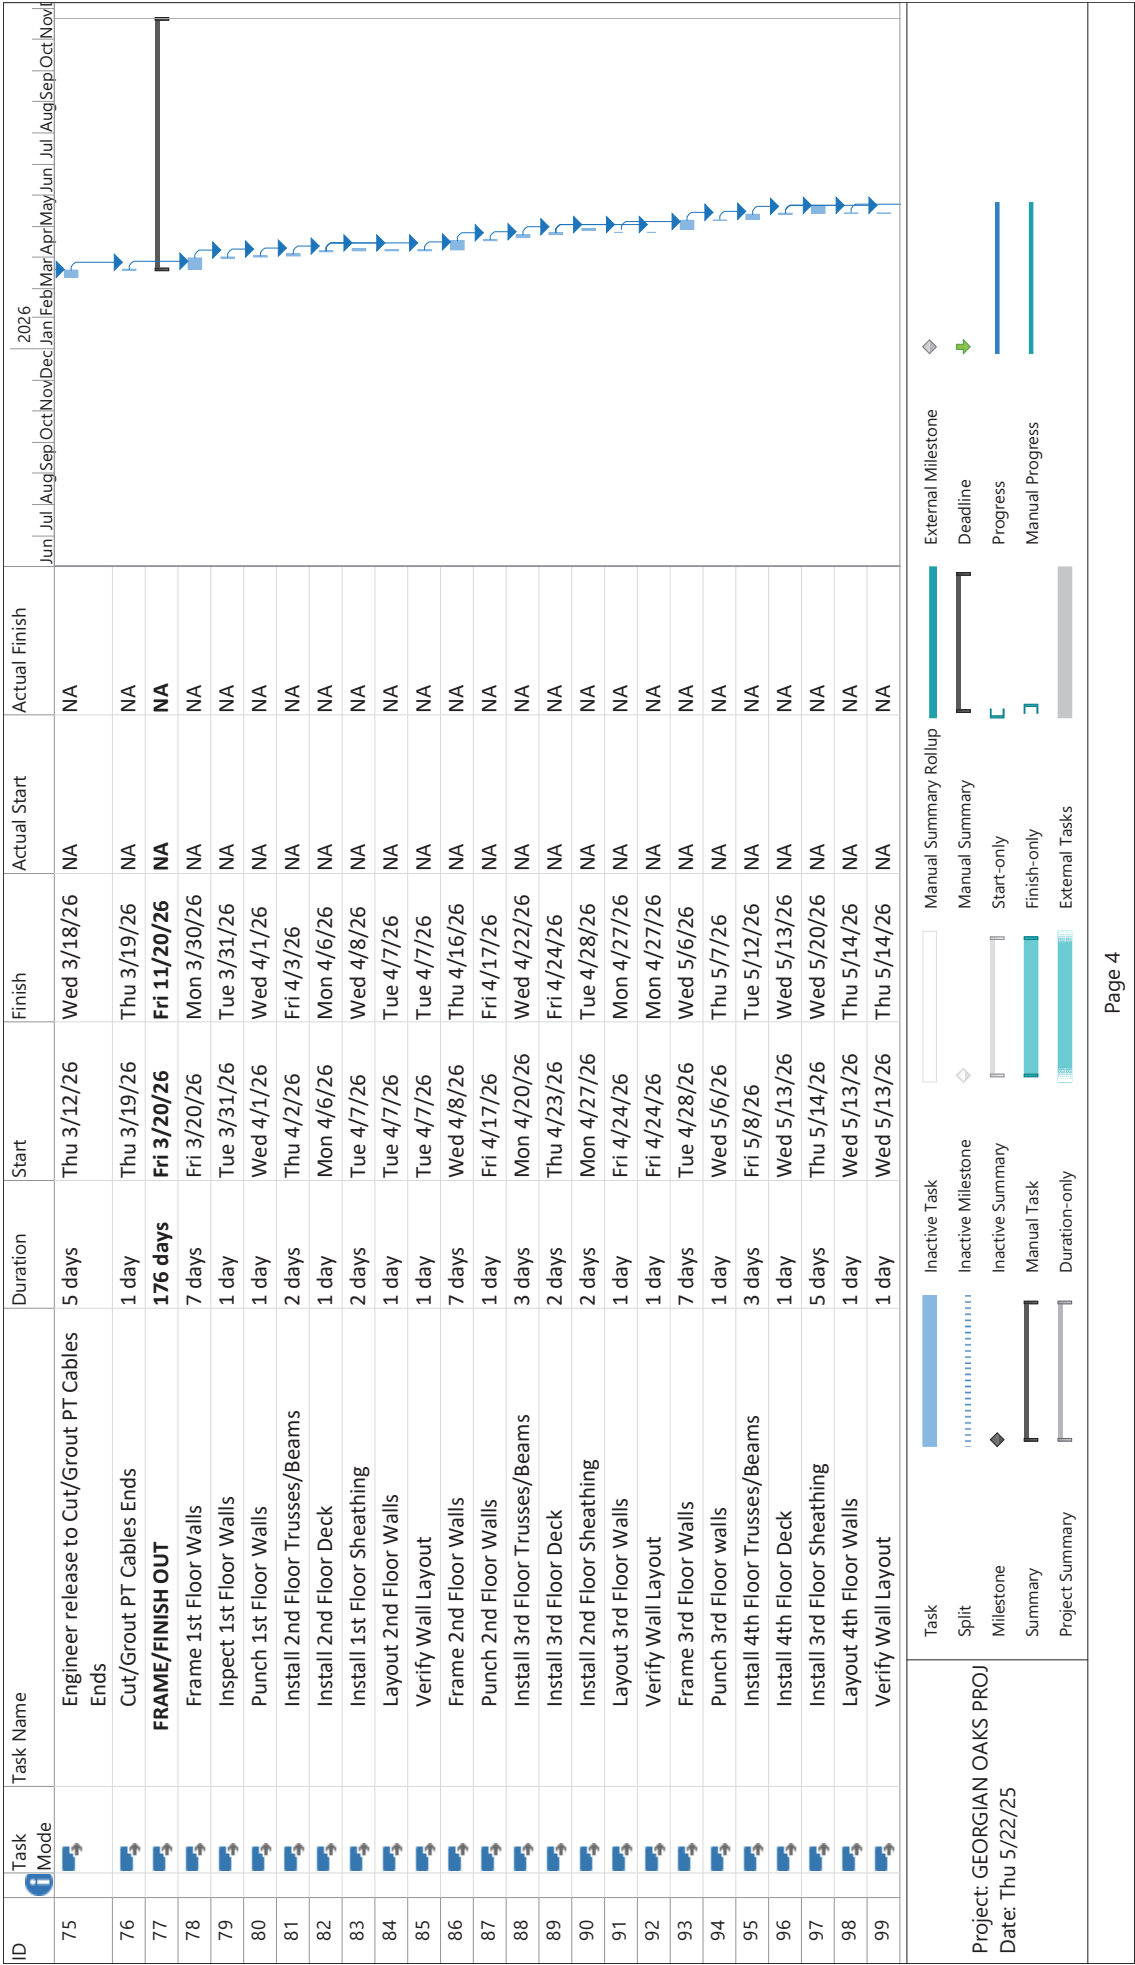

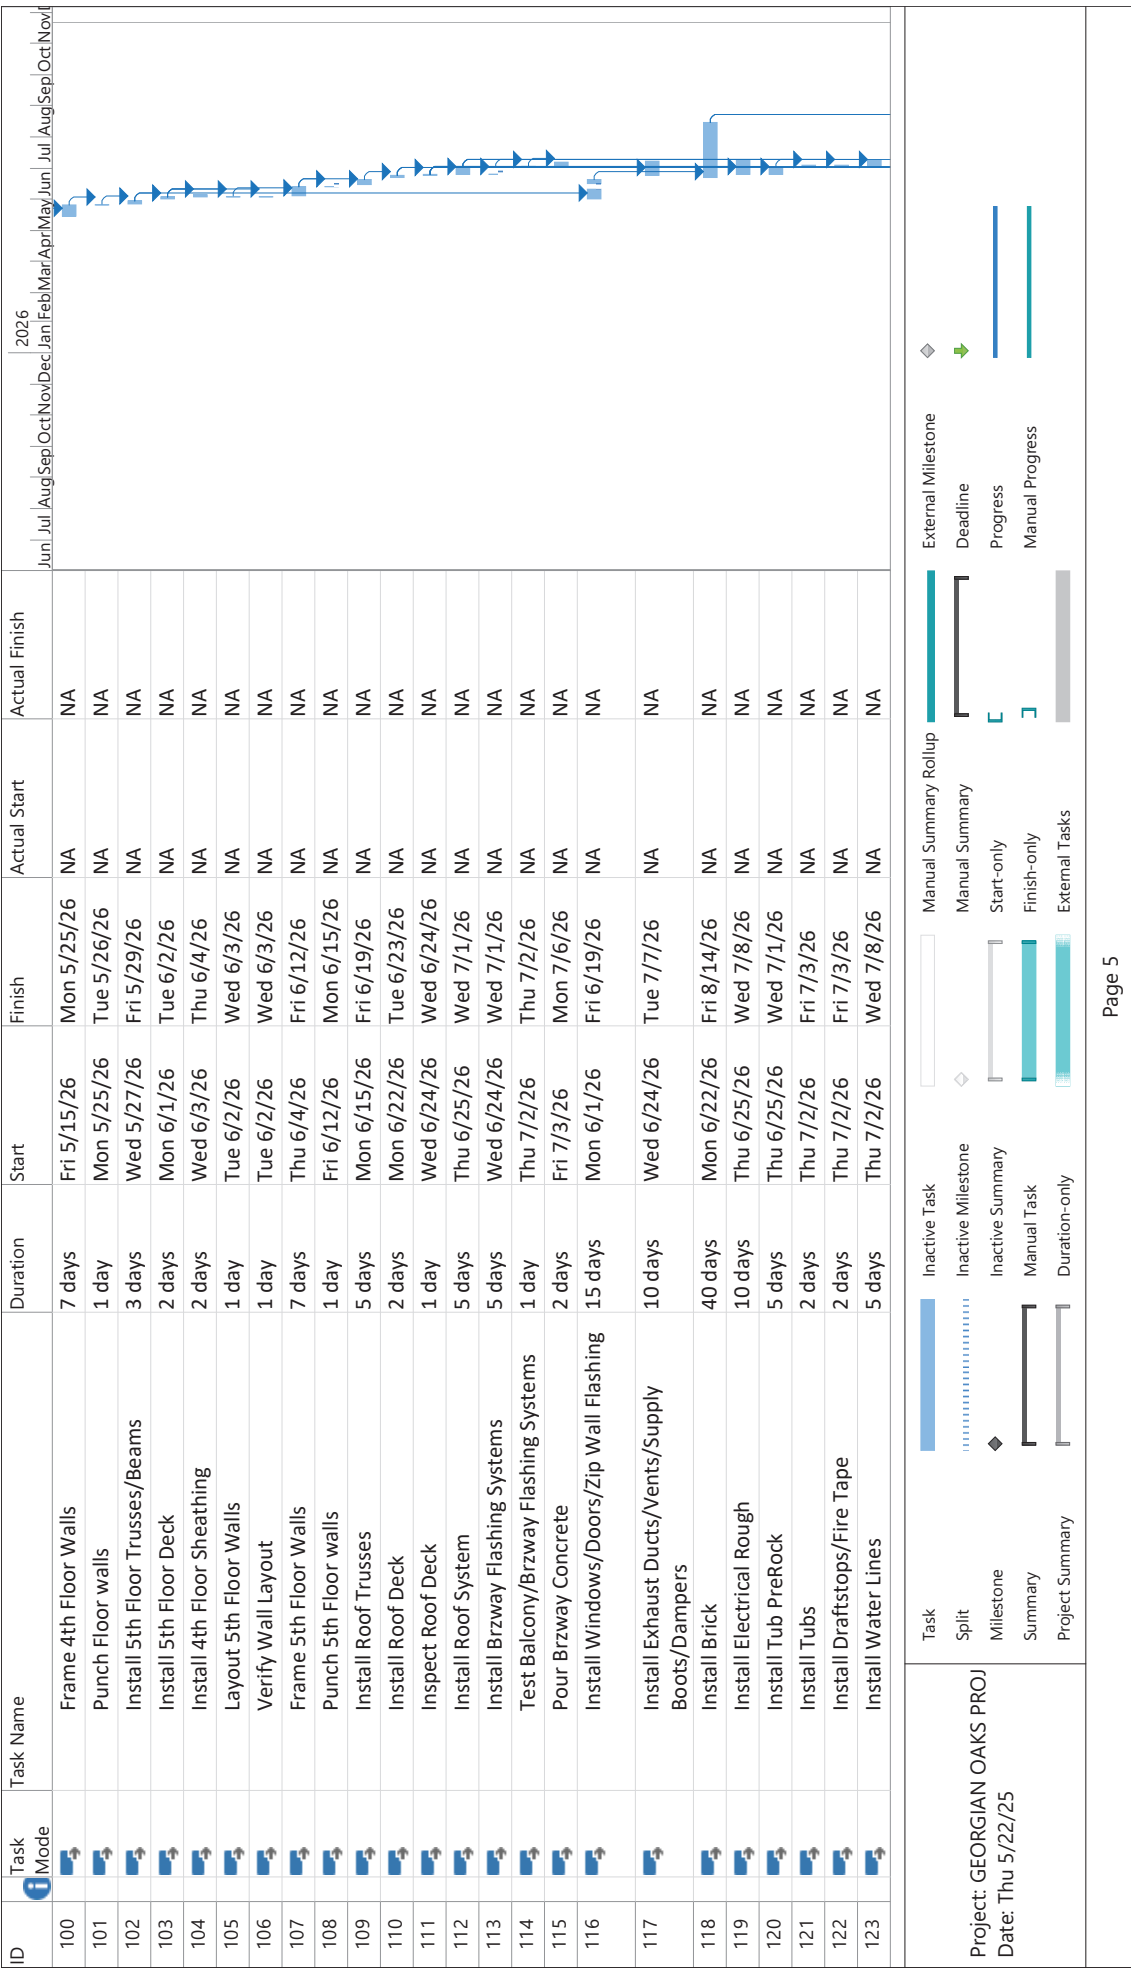

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish		2026 JunJulAugSepOctNovDecJanFebMarAprMayJunJulAugSepOctNov
124		Install Fire Sprinkler Rough-In	5 days	Wed 6/24/26	Tue 6/30/26	NA	NA		
125		Install Low Voltage Wire	1 day	Thu 7/2/26	Thu 7/2/26	NA	NA		
126		Install Air Handlers/Ducts/Vent Boots	5 days	Thu 6/25/26	Wed 7/1/26	NA	NA		
127		Poly Seal Bldg	2 days	Thu 7/2/26	Fri 7/3/26	NA	NA		
128		Fire Sprinkler Inspection	1 day	Wed 7/1/26	Wed 7/1/26	NA	NA		
129		MEP Inspection	1 day	Thu 7/2/26	Thu 7/2/26	NA	NA		
130		Framing Inspection	1 day	Fri 7/3/26	Fri 7/3/26	NA	NA		
131		Install Insulation	5 days	Mon 7/6/26	Fri 7/10/26	NA	NA		
132		Insulation Inspection	1 day	Mon 7/13/26	Mon 7/13/26	NA	NA		
133		Install Sheetrock	10 days	Tue 7/14/26	Mon 7/27/26	NA	NA		
134		Tape/Bed/Texture	10 days	Tue 7/28/26	Mon 8/10/26	NA	NA		
135		Pour gypcrete	1 day	Tue 8/11/26	Tue 8/11/26	NA	NA		
136		Install Trim & Doors	10 days	Wed 8/12/26	Tue 8/25/26	NA	NA		
137		Paint Interiors	10 days	Wed 8/26/26	Tue 9/8/26	NA	NA		
138		Electrical Trim Out	5 days	Wed 8/26/26	Tue 9/1/26	NA	NA		
139		Low Voltage Trim Out	5 days	Wed 9/9/26	Tue 9/15/26	NA	NA		
140		Electrical Inspection	1 day	Wed 9/2/26	Wed 9/2/26	NA	NA		
141		Set Electrical Meters	1 day	Thu 9/3/26	Thu 9/3/26	NA	NA		
142		Install Tub Surrounds	5 days	Mon 9/7/26	Fri 9/11/26	NA	NA		
143		HVAC Trim/Set Condensors	5 days	Wed 9/9/26	Tue 9/15/26	NA	NA		
144		HVAC Start Up	5 days	Fri 9/4/26	Thu 9/10/26	NA	NA		
145		Fire Sprinkler/Alarm Trim Out	5 days	Wed 9/9/26	Tue 9/15/26	NA	NA		
146		Cabinet/Countertop Delivery	5 days	Wed 9/9/26	Tue 9/15/26	NA	NA		
147		Install Cabinets & Countertops	10 days	Wed 9/16/26	Tue 9/29/26	NA	NA		
148		Install Tile Backsplashes	3 days	Wed 9/30/26	Fri 10/2/26	NA	NA		

Project: GEORGIAN OAKS PROJ

Date: Thu 5/22/25

Task

Inactive Task
 Inactive Milestone
 Inactive Summary
 Manual Task
 Duration-only

Split
 Milestone
 Summary
 Project Summary

Manual Summary Rollup

Manual Summary
 Start-only
 Finish-only
 External Tasks

External Milestone

Deadline
 Progress
 Manual Progress

Page 6

ID	Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish		2026 Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec
149		Install Vinyl Floors	10 days	Mon 9/28/26	Fri 10/9/26	NA	NA		
150		Install Second Trim	5 days	Tue 10/13/26	Mon 10/19/26	NA	NA		
151		Drywall Punch	10 days	Wed 9/2/26	Tue 9/15/26	NA	NA		
152		Paint Second Trim / Punch	5 days	Wed 9/16/26	Tue 9/22/26	NA	NA		
153		Install Minor Appliances	1 day	Mon 10/5/26	Mon 10/5/26	NA	NA		
154		Plumbing Trim Out	10 days	Fri 10/9/26	Thu 10/22/26	NA	NA		
155		Install mirrors	2 days	Wed 9/30/26	Thu 10/1/26	NA	NA		
156		Install door and bathroom hardware	5 days	Wed 9/9/26	Tue 9/15/26	NA	NA		
157		Receive and install major appliances (refrigerator & ranges)	2 days	Fri 10/23/26	Mon 10/26/26	NA	NA		
158		Final touch up paint	5 days	Fri 10/23/26	Thu 10/29/26	NA	NA		
159		Install gutters and down spouts	3 days	Mon 8/17/26	Wed 8/19/26	NA	NA		
160		Install exterior signage	1 day	Mon 8/17/26	Mon 8/17/26	NA	NA		
161		Hole in the door energy inspection	2 days	Fri 10/30/26	Mon 11/2/26	NA	NA		
162		Final clean	5 days	Fri 10/30/26	Thu 11/5/26	NA	NA		
163		MEP Final Inspections	4 days	Fri 10/23/26	Wed 10/28/26	NA	NA		
164		Fire Sprinkler/Alarm Final Inspection	4 days	Fri 10/23/26	Wed 10/28/26	NA	NA		
165		Owner First Walk	1 day	Fri 11/6/26	Fri 11/6/26	NA	NA		
166		Final Punch/Reclean	10 days	Mon 11/9/26	Fri 11/20/26	NA	NA		
167		Owner Acceptance	0 days	Fri 11/20/26	Fri 11/20/26	NA	NA		

Project: GEORGIAN OAKS PROJ

Date: Thu 5/22/25

Task

Inactive Task

Manual Summary Rollup

External Milestone

Page 7
